


Critical Path Schedule for Masonry vs. Tilt (Evans High School - Replacement School)

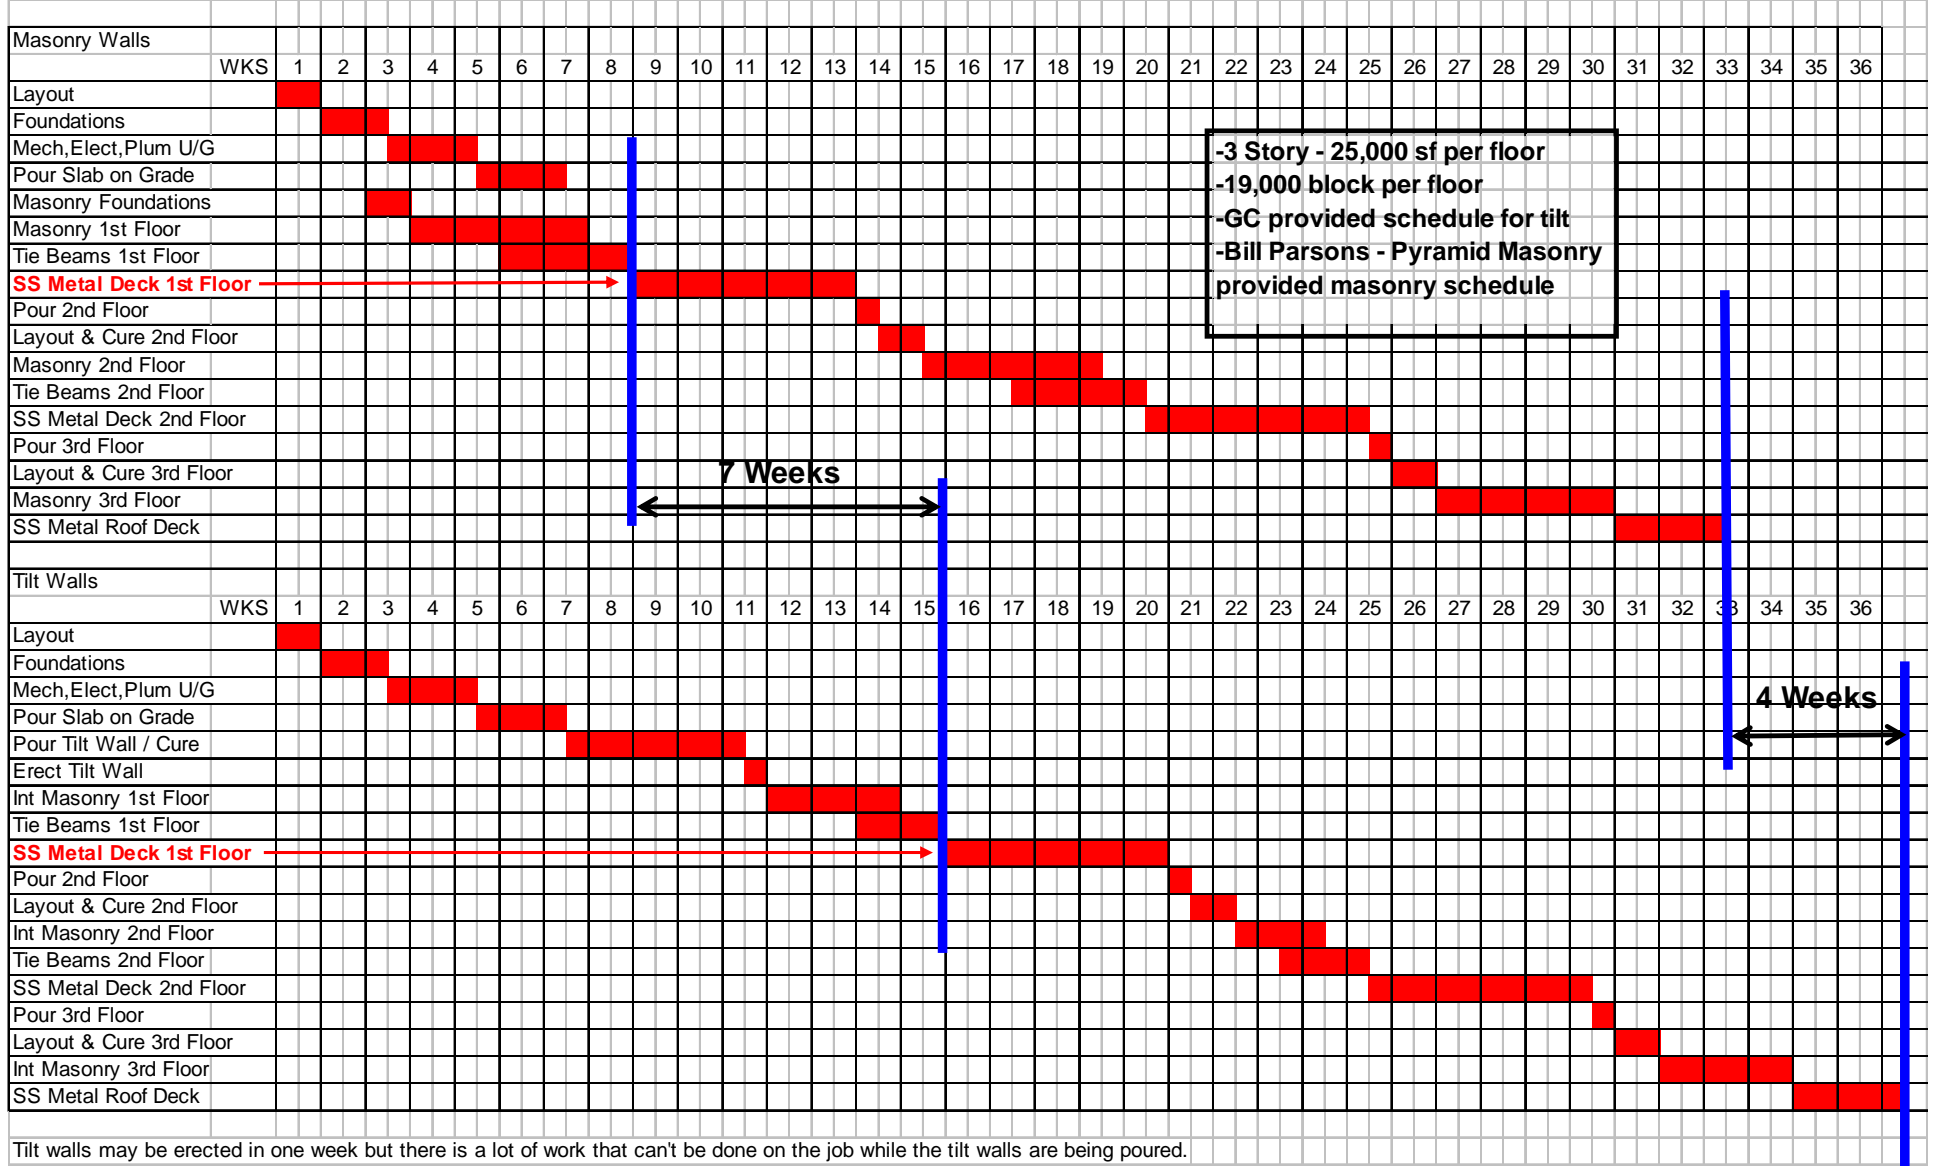

-3 Story - 25,000 sf per floor
 -19,000 block per floor
 -GC provided schedule for tilt
 -Bill Parsons - Pyramid Masonry provided masonry schedule

7 Weeks

4 Weeks

Tilt walls may be erected in one week but there is a lot of work that can't be done on the job while the tilt walls are being poured.
 After the tilt walls are erected there's still slab work that has to be done that is not on the schedule.
 Casting slabs over the column box-outs, stub-ups, and sloped floors have to be removed and repoured.
 Pour-strip around entire perimeter has to be poured to complete the slab.
 Casting slabs around the exterior of the building have to be removed.

Data compiled by:
 Bill Parsons
